ID	Task Name	Duration	Start	Finish
1	**PHASE IB**	**8 days**	**Tue 12/15/15**	**Thu 12/24/15**
2	SIDEWALK & RAMPS	5 days	Tue 12/15/15	Mon 12/21/15
3	BACKFILL	2 days	Tue 12/22/15	Wed 12/23/15
4	STRIPING & SIGNAGE	1 day	Thu 12/24/15	Thu 12/24/15
5	SWITCH TRAFFIC	1 day	Thu 12/24/15	Thu 12/24/15
6				
7	**PHASE 2A**	**46 days**	**Fri 12/25/15**	**Fri 2/26/16**
8	CHRISTMAS HOLIDAYS (NO WORK)	6 days	Fri 12/25/15	Sun 1/3/16
9	CLOSE NORTH SIDE	1 day	Mon 1/4/16	Mon 1/4/16
10	STORM DRAIN	12 days	Tue 1/5/16	Wed 1/20/16
11	EXCAVATION	5 days	Thu 1/21/16	Wed 1/27/16
12	LIME STABILIZATION	4 days	Thu 1/28/16	Tue 2/2/16
13	CONCRETE PAVING	5 days	Wed 2/3/16	Tue 2/9/16
14	INTERSECTIONS	5 days	Wed 2/10/16	Tue 2/16/16
15	INLET TOPS	2 days	Wed 2/10/16	Thu 2/11/16
16	DRIVEWAYS	5 days	Wed 2/10/16	Tue 2/16/16
17	SIDEWALK & RAMPS	5 days	Wed 2/17/16	Tue 2/23/16
18	BACKFILL	2 days	Wed 2/24/16	Thu 2/25/16
19	SWITCH TRAFFIC	1 day	Fri 2/26/16	Fri 2/26/16
20				
21	**PHASE 2B**	**23 days**	**Mon 2/29/16**	**Wed 3/30/16**
22	EXCAVATION	4 days	Mon 2/29/16	Thu 3/3/16
23	LIME STABILIZATION	4 days	Fri 3/4/16	Wed 3/9/16
24	CONCRETE PAVING	5 days	Thu 3/10/16	Wed 3/16/16
25	INTERSECTIONS	5 days	Thu 3/17/16	Wed 3/23/16
26	INLET TOPS	2 days	Thu 3/17/16	Fri 3/18/16
27	DRIVEWAYS	5 days	Thu 3/17/16	Wed 3/23/16
28	SIDEWALK & RAMPS	5 days	Thu 3/17/16	Wed 3/23/16
29	BACKFILL	2 days	Thu 3/24/16	Fri 3/25/16
30	STRIPING & SIGNAGE	2 days	Mon 3/28/16	Tue 3/29/16
31	SWITCH TRAFFIC	1 day	Wed 3/30/16	Wed 3/30/16

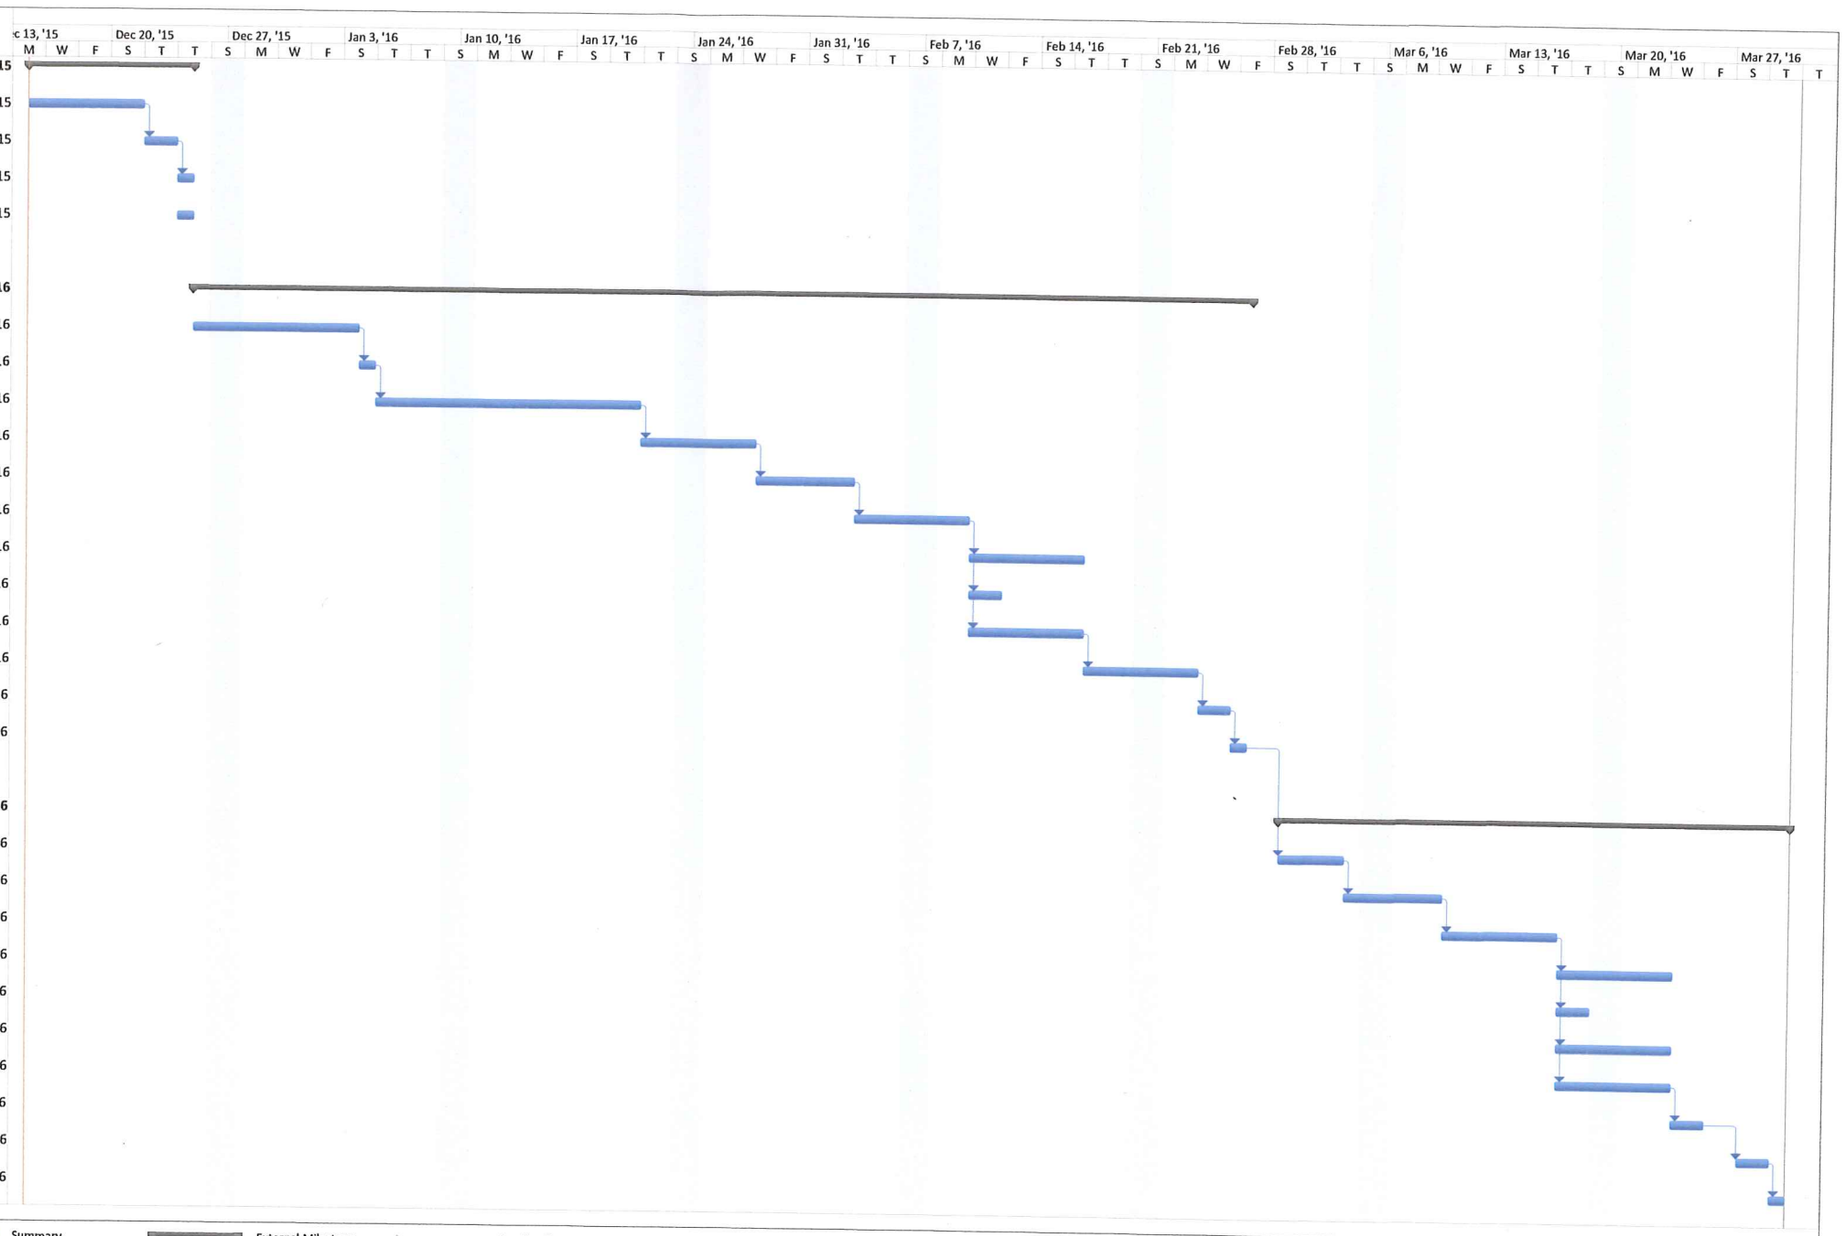

Project: Bethel & Coppell 121515
Date: Tue 12/15/15

Task		Summary		External Milestone		Inactive Summary		Manual Summary Rollup		Finish-only	
Split		Project Summary		Inactive Task		Manual Task		Manual Summary		Deadline	
Milestone		External Tasks		Inactive Milestone		Duration-only		Start-only		Progress	
